


Giant Mine Remediation Environmental Assessment Timeline EA0809-001

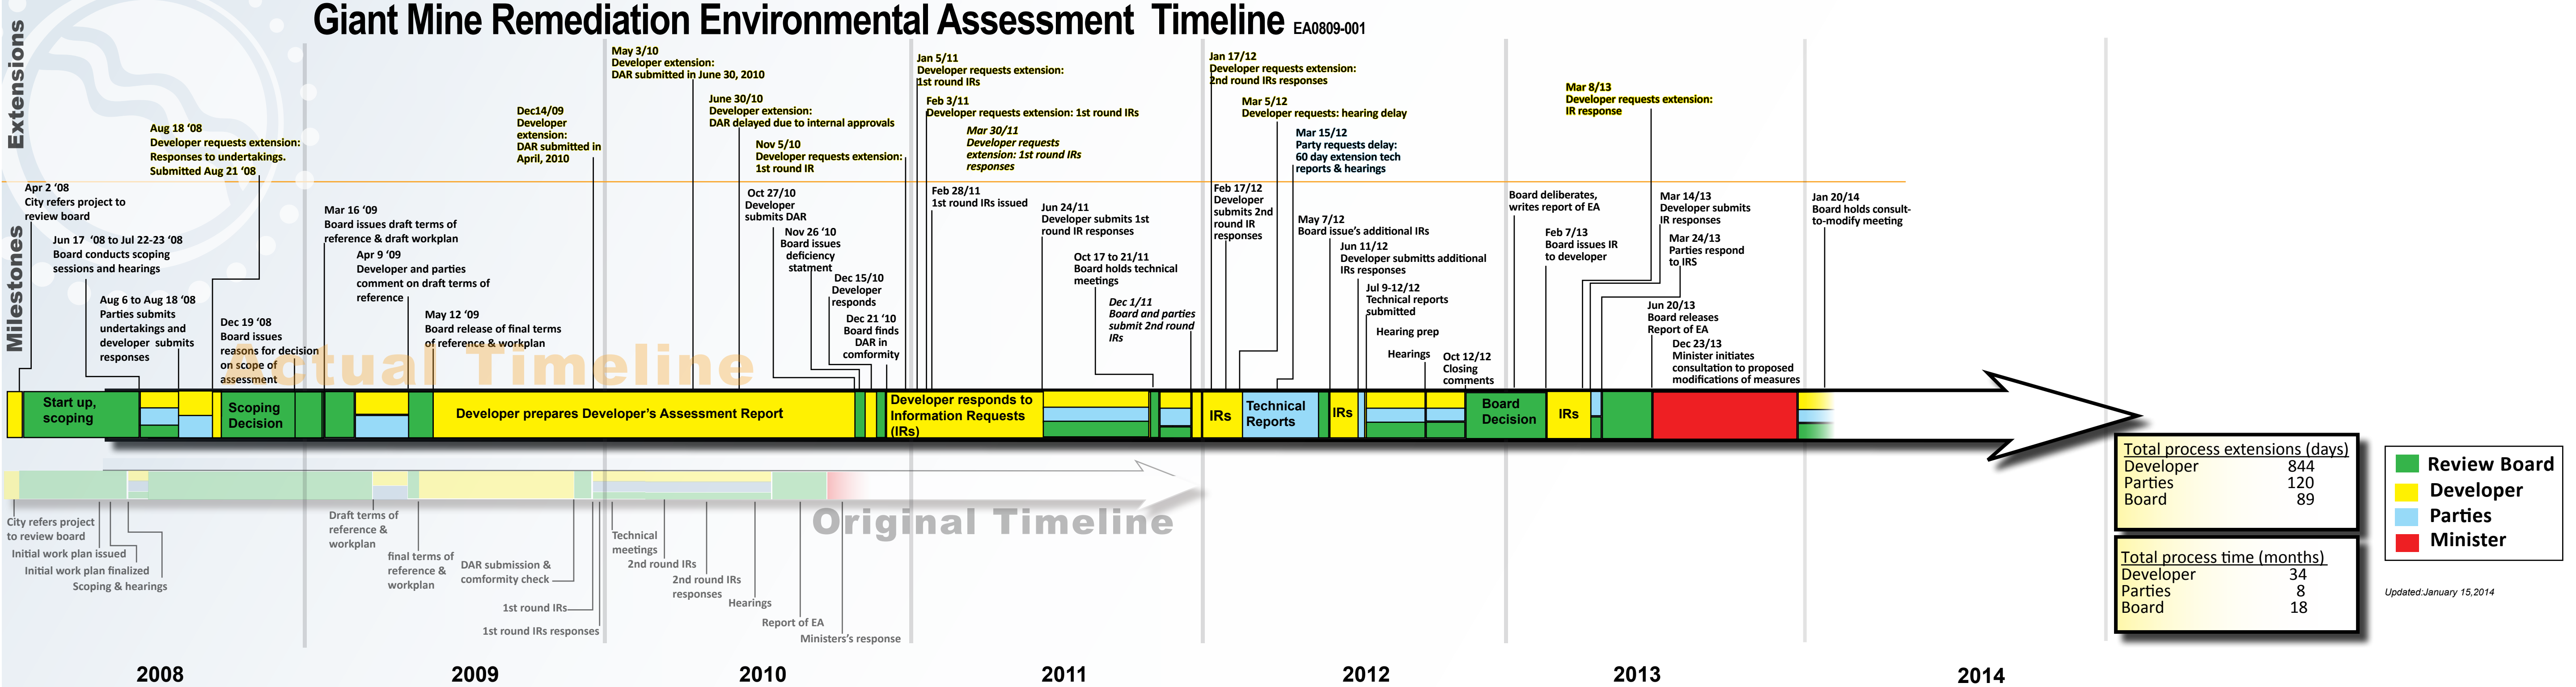

Extensions

Milestones

Actual Timeline

Original Timeline

Total process extensions (days)	
Developer	844
Parties	120
Board	89

Total process time (months)	
Developer	34
Parties	8
Board	18

- Review Board
- Developer
- Parties
- Minister

Updated: January 15, 2014

Aug 18 '08
Developer requests extension: Responses to undertakings. Submitted Aug 21 '08

Apr 2 '08
City refers project to review board

Jun 17 '08 to Jul 22-23 '08
Board conducts scoping sessions and hearings

Aug 6 to Aug 18 '08
Parties submits undertakings and developer submits responses

Mar 16 '09
Board issues draft terms of reference & draft workplan

Apr 9 '09
Developer and parties comment on draft terms of reference

Dec 19 '08
Board issues reasons for decision on scope of assessment

May 12 '09
Board release of final terms of reference & workplan

Dec 14/09
Developer extension: DAR submitted in April, 2010

June 30/10
Developer extension: DAR delayed due to internal approvals

Nov 5/10
Developer requests extension: 1st round IR

Oct 27/10
Developer submits DAR

Nov 26 '10
Board issues deficiency statement

Dec 15/10
Developer responds

Dec 21 '10
Board finds DAR in conformity

Jan 5/11
Developer requests extension: 1st round IRs

Feb 3/11
Developer requests extension: 1st round IRs

Mar 30/11
Developer requests extension: 1st round IRs responses

Feb 28/11
1st round IRs issued

Jun 24/11
Developer submits 1st round IR responses

Oct 17 to 21/11
Board holds technical meetings

Dec 1/11
Board and parties submit 2nd round IRs

Jan 17/12
Developer requests extension: 2nd round IRs responses

Mar 5/12
Developer requests: hearing delay

Mar 15/12
Party requests delay: 60 day extension tech reports & hearings

Feb 17/12
Developer submits 2nd round IR responses

May 7/12
Board issue's additional IRs

Jun 11/12
Developer submits additional IRs responses

Jul 9-12/12
Technical reports submitted

Hearings prep

Hearings

Oct 12/12
Closing comments

Mar 8/13
Developer requests extension: IR response

Board deliberates, writes report of EA

Feb 7/13
Board issues IR to developer

Jun 20/13
Board releases Report of EA

Dec 23/13
Minister initiates consultation to proposed modifications of measures

Mar 14/13
Developer submits IR responses

Mar 24/13
Parties respond to IRs

Jan 20/14
Board holds consult-to-modify meeting

2008

2009

2010

2011

2012

2013

2014
